

STATUS OF ON-GOING RIDF PROJECTS FOR 2018-19

EASTERN ZONE, PWD



SUMMARY OF ON-GOING RIDF PROJECTS AS ON 09.08.2018

(Fin. Fig. in Lakhs)

									(2 1110 1	ig. iii Lamis)
Sl. No.	Sub-Head	Nos of scheme	Total Sanctioned amount	Funds released till March '18	Progressive expdr till 03/2018	Funds released during 2018-19	Expdr during 2018-19	Cumm. expdr till	UC submitted	Remarks
1	2	3	4	5	6	7	8	9	10	11
1	RIDF XIX 2013-14	2	1215.38	1215.25	1214.83			1214.83	1214.83	PCR of both schemes by 8/18
2	RIDF XX 2014-15	3	2808.23	2367.19	2199.18	468.01		2199.18	2199.18	PCR of 2 schemes by 8/18; Bal 1 no. by 3/19
3	RIDF XXI 2015-16	5	4994.55	4335.10	4029.32	376.19		4029.32	4029.32	PCR of 1 no. by 8/18; Bal 4 nos by 3/19
4	RIDF XXII 2016-17	3	3500.00	943.25	477.00	966.24		477.00	477.00	PDC by 3/20
5	RIDF XXIII 2017-18	7	8680.00	999.00	0.00	1348.00		0.00	0.00	PDC by 3/21
	Total	20	21198.16	9859.79	7920.33	3158.44	0	7920.33	7920.33	



PHYSICAL TARGETS & ACHIEVEMENTS UNDER RIDF DURING 2018-19 UNDER EASTERN ZONE

Sl. No.	Sub-Head	Unit	Target	Achievement	Percentage of Achievement
1	2	3	4	5	6
1	Earth work	Km	22.37		
2	GSB/WBM-I	Km	15.45		
3	WBM-II	Km	11.14		
4	WBM-III	Km	16.88		
5	Black Topping	Km	33.43		
6	S/Cul (various span)	No.	45		
7	R & B Wall	Mtr.	425.00		
8	Pucca Drain	Km	7.92		
9	CC Pavement	Km	0.48		
10	RCC/Steel Bridge	No./Mtr	1/80.00		
11	River Training Works	Mtr.	225.00		



RIDF- XIX (2013-14)

- 1. C/o Road from Namsai to Jaipur i/c RCC Bridge
- 2. <u>C/o Road from 7th Km point of NH-52 to Mime (SH: C/o steel bridge over river Tiyang (60 Mtr)</u>



NAME OF PROJECT: C/o Road from Namsai to Joypur i/c RCC Bridge.

SANCTION NO. & DATE: NB/SPD/434/RIDF-XIX/Ar.P/135/PSC/Project No. 89-95/13-14, dtd. 31/07/2013

For Rs. 801.00 lakhs (CS: Rs. 720.90 lakhs & SS: Rs. 80.10 lakhs)

(Financial figures in lakhs)

Cumulative		Scope of W	Vork		Progre Achievem 3/1	ent upto	Target 2018-1		Achiever During 20		Cumula Achieveme 3/201	nt upto	UC Status/
Release	d	Phy.		Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Remarks
			Rate	r III.	Fily.	FIII.	Fily.	riii.	Fily.	riii.	Fily.	riii.	
LC (2013-14)	216.70	1) Earth work-4.94 Km	6.55		4.94 Km								
LC (2014-15)	332.78	2) G.S.B4.94 Km	15.42		4.94 Km								
LC (2015-16)	171.42	3) WBM-II-4.94 Km	15.18		4.94 Km								
SS (2017-18)	80.10	4) WBM-III-4.94 Km	12.40		4.94 Km								UC Submitted for Rs 800.58 lakhs
Total	801.00	5) Black Topping-4.94 Km	14.40		4.94 Km								
		6) S/Cul 1. mtr span-5 Nos 4.09		801.00	5 Nos	800.58						-	PCR to be submitted
		7) S/Cul 2. mtr span-4 Nos	11.45		4 Nos								by 8/18
		8) RCC Bridge 40. mtr span-1 No	406.00		Bridge 95%		100% Completion						



C/O ROAD FROM NAMSAI TO JOYPUR i/c RCC BRIDGE





Road work 100% completed



C/O ROAD FROM NAMSAI TO JOYPUR i/c RCC BRIDGE



Bridge work 90% completed

NAME OF PROJECT: C/o Road from 7th Km point of NH-52 to Mime (SH: C/o steel bridge over river Tiyang (60 Mtr)

SANCTION NO. & DATE: NB/SPD/434/RIDF-XIX/Ar.P/135/PSC/Project No. 89-95/13-14, dtd. 31/07/2013

For Rs. 414.38 lakhs (CS: Rs. 372.96 lakhs & SS: Rs. 41.42 lakhs)

(Financial figures in lakhs)

Cumulative F		Scope o	of Work		Progress Achievement u		Target 2018-19		Achievement During 2018-19		Cumulative Achievement upto 3/2019		UC Status/
Released		Phy.		Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Phy.	Fin.	Remarks
			Rate	FIII.	T ily.	riii.	T my.	riii.	T fly.	riii.	T fly.	rin.	
LC (2013-14)	111.83	1) Sub-	147.61		Sub-								
LC (2014-15)	50.00	structure-1 Job			structure completed								
LC (2015-16)	211.00												
SS (2017-18)	41.42												
Total	414.25												UC Submitted
		2) Super- structure-1 Job	172.00	44.40	Lunching compltd	414.25	100% Completion						for Rs 414.25
		3) Approach road-450 mtr	40.22	414.18	450								lakhs PCR by 8/18
			42.38		1561								



C/O ROAD FROM 7TH KM POINT OF NH-52 TO MIME (SH : C/O STEEL BRIDGE OVER RIVER TIYANG (60 M SPAN)



Bridge work 90% completed



RIDF-XX (2014-15)

- 1. <u>C/o Steel Bridge (Span 80 Mtr) on Haju river on road from NH-52</u>

 <u>BRTF Road to Bhekuliang in Lohit District</u>
- 2. C/o Road from New Jenthu to Jona-III in Namsai District
- 3. C/o Road from Emphum to Injo via Tingua and Insa in Namsai

 District

NAME OF PROJECT: C/o Bridge (Span 80 Mtr) over Haju river on NH-52 BRTF Road to Bhekuliang, Tezu.

SANCTION NO. & DATE: NB/SPD/951/RIDF-XX(Ar.P)/148/PSC/Project No. 113/2014-15, dtd. 18/03/2015

For Rs. 742.23 lakhs (CS: Rs. 668.01 lakhs & SS: Rs. 74.22 lakhs)

(Financial figures in lakhs)

Cumulative Fu	ınds Released	Scope of W	orks		Progre Achievemo 03/ 20	ent upto	Target 2	2018-19	Achiev during 2		Cumu Achiev upto 03	ement	UC Status/ Remarks
	<u> </u>	Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2017-18) LC(2018-19) Fund		1) Sub-structure- 3 Nos 2) Super-structure- 80 mtr 3) RCC Decking- 80 mtr	315.08 61.68	742.23	Well steining for 2 Nos Abut & 1 pier upto 5.65 m compltd.	200.00	80.00	468.01					UC submitted
surrendered during 2017- 18		inu i						10001					Rs. 200.00 lakhs
Total	668.01	4) Approach work- 0.28 Km	44.59				0.28						
		5) Wing Wall- 4 Nos	37.49				4						
		6) Protection work- 400 mtr	96.12		In progress		400.00						



C/o bridge on NH-52 BRTF road to Bhekuliang, Tezu, SH:- Steel composite bridge over river Haju in Lohit District of Arunachal Pradesh.





Abutment - Left Bank well sinking in progress

Abutment-Right Bank well sinking in progress



C/o bridge on NH-52 BRTF road to Bhekuliang, Tezu, SH:- Steel composite bridge over river Haju in Lohit District of Arunachal Pradesh.



Pier - well sinking in progress



Protection work in progress

NAME OF PROJECT: C/o Road from New Jenthu to Jona-III in Namsai District.


SANCTION NO. & DATE: NB/SPD/974/RIDF-XX(Ar.P)/149th PSC/Project No. 118/2014-15, dtd. 27/03/2015

SANCTION AMOUNT: Rs. 666.00 lakhs (CS: Rs. 599.40 lakhs & SS: Rs. 66.60 lakhs) (Financial figures in lakhs)

Cumulative Release		Scope of W	orks		Progres Achieveme 03/ 20	ent upto	Target 201	8-19	Achiev during 2		Cumu Achiev upto 0	ement	UC Status/ Remarks
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2015-16)	250.00	1) Earth work- 2.64 Km	3.64		2.64								
LC (2016-17)	250.00	2) Preparation of sub- grade- 2.64 Km	2.98		2.64								
LC(2017-18)	99.40	3) GSB- 2.64 Km	20.75		2.64								
SS (2017-18)	47.98	4) WBM- II- 2.64 km	17.63		2.64								
Total	647.38	5) WBM- III- 2.64 Km	12.45		2.64		100%						UC
		6) Carpetting- 2.64 Km	16.00	666.00	2.64	647.38	Completion (Liability	18.62					submitted Rs. 647.38
		7) S/Cul 1m span- 3 Nos	4.80		3		clearance)						lakhs
		8) S/Cul 2m span- 3 Nos	10.62		3								
		9) S/Cul 4m span- 2 Nos	20.46		2								
		10) Steel Bridge (40 mtr span)- 1 Nos	2.92		Launching of bridge compltd								



C/O ROAD FROM NEW JENGTHU TO JONA-III IN NAMSAI DISTRICT (RCC BRIDGE 40 M SPAN)

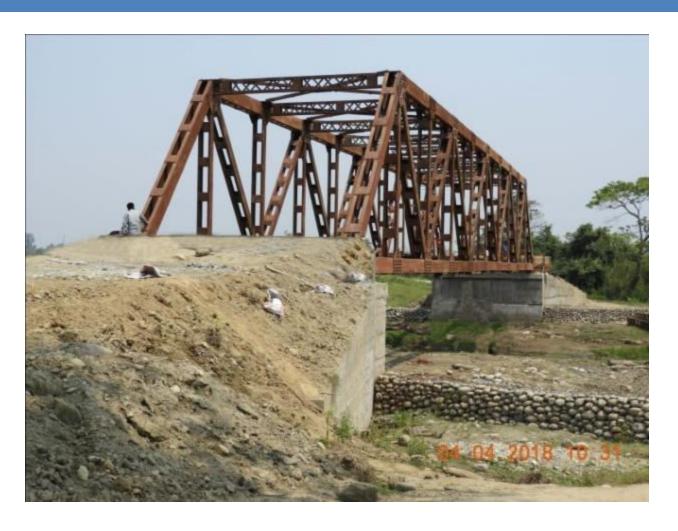





S/Culvert 4.00m span at 0.90 Km.



S/Culvert 1.00m span at 1.50 Km.

C/O ROAD FROM NEW JENGTHU TO JONA-III IN NAMSAI DISTRICT.



C/O ROAD FROM NEW JENGTHU TO JONA-III IN NAMSAI DISTRICT.





CH-0.30 Km

CARPETTING



NAME OF PROJECT: C/o Road from Emphum to Injo via Tingua and Insa in Namsai District

SANCTION NO. & DATE: NB/SPD/974/RIDF-XX(Ar.P)/149th PSC/Project No. 118-119/2014-15, dtd. 27/03/2015

For Rs. 1400.00 lakhs (CS: Rs. 1260.00 lakhs & SS: Rs. 140.00 lakhs)

(Financial figures in lakhs)

Cumulativ Release		Scope of Wo	Progressive Achievement upto 03/ 2018		Target 2018-19		Achievement during 2018-19		Cumulative Achievement upto 03/2019		UC Status/ Remarks		
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2015- 16)	500.00	1) Earth work- 7.00 Km	21.29		7.00								
LC (2016- 17)	400.00	2) GSB- 7.00 Km	20.00		7.00								
LC (2017- 18)	360.00	3) WBM- II- 18.00 Km	16.00		18.00								
SS (2017-18)	91.80	4) WBM- III- 18.00 Km	12.13	12.13	18.00								UC
Total	1351.80	5) Carpetting- 18.00 Km	16.84	1400.00	18.00	1351.80	100%	48.20					submitted Rs.
		6) S/Cul 1m span- 31 Nos	4.61		31		Completion						1351.80 lakhs
		7) S/Cul 2m span- 7 Nos	10.21		7								
		8) S/Cul 6m span- 1 No	21.75		1								
		9) Cause way- 1 No	15.92										



C/O ROAD FROM EMPHUM TO INJO VIA TINGUA & INSA IN NAMSAI DISTRICT.





CH. 7.70 KM (1.0 M SPAN)



CH. 5.50 KM (1.0 M SPAN)



CULVERTS

CH. 12.15 KM (6.0 M SPAN)



C/o Road & Bridge from Emphum to Lunka village via Munglang village (10km)



Earth work at Ch:- 0.80 Km

C/O ROAD FROM EMPHUM TO INJO VIA TINGUA & INSA IN NAMSAI DISTRICT.



Ch. 13.30 Km (2.0 m span)



WBM



Ch. 20.90Km (2.0 m span)



Ch:- 4.50 KM. WBM



C/O ROAD FROM EMPHUM TO INJO VIA TINGUA & INSA IN NAMSAI DISTRICT.



Ch:- 3.60 Km



Ch:- 15.10 Km.

A CHALL PROPERTY.

C/O ROAD FROM EMPHUM TO INJO VIA TINGUA & INSA IN NAMSAI DISTRICT



Ch:- 4.50 Km

Ch:- 16.20 Km





S/Culvert 6.00m span at Ch:- 12.15 Km




S/Culvert 2.00m span at Ch:- 0.60 Km



C/O ROAD FROM EMPHUM TO INJO VIA TINGUA & INSA IN NAMSAI DISTRICT.



Ch:- 14.50 Km.

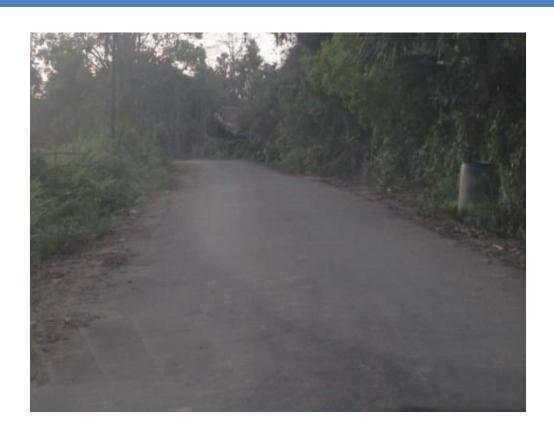

Black Topping



RIDF-XXI (2015-16)

- 1. <u>C/o internal link roads under Diyun Administrative Hq. in Changlang</u>

 <u>District</u>
- 2. C/o Approach Road from CO Hq. Dadam to Muktowa-II in Tirap
- 3. <u>C/o RCC Bridge (Span 24 Mtr) at 11 Km on Wakro Deban road in Wakro Circle, Namsai District</u>
- 4. <u>C/o Road from Votnu village to Khanu village, Wakka Circle in Longding District</u>
- 5. C/o Road from Chattong to Kamnu via Chopsa in Longding District

NAME OF PROJECT: C/o internal link roads under Diyun Administrative Hq. in Changlang District

SANCTION NO. & DATE: NB.AR/629/SPD-3/2015-16, dated. 04/12/2015,

For Rs. 974.55 lakhs (CS: Rs. 877.10 lakhs & SS: Rs. 97.45 lakhs)

(Financial figures in lakhs)

Cumulative Release		Scope of Wo	Progressive Achievement upto 03/ 2018		Target 2018-19		Achievement during 2018-19		Cumulative Achievement upto 03/2019		UC Status/ Remarks		
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2016-17)	300.00	1) Earth work- 11.00 Km	10.94		11.00								
LC (2017-18)	524.00	2) GSB-I- 11.00 Km	20.20		11.00			_					
LC (2018-19)	53.10	3) WBM-II- 11.00 Km	9.78	_	10.06	_	0.94	_		_		_	UC submitted
Total	877.10	4)WBM-III- 11.00 Km	9.78	_	9.80	_	1.20	_					Rs. 824.00 lakhs
		5) Black topping- 11.00 Km	12.96	974.55		824.00	11.00	53.10					Full physical
		6) S/Cul 1 m span- 17 Nos	9.91		17								targets in anticipation of receipt of
		7)S/Cul 6 m span- 2 Nos	36.92		2								state share.
		8) Informatory sign board & Km stone- 11.00 Km	0.23				100%						



CONSTRUCTION OF INTERNAL LINK ROADS UNDER DIYUN ADMINISTRATIVE HQ IN CHANGLANG DISTRICT: (11.00 KM)





EMBANKMENT FILLING







GSB







GSB at Kumchaikha Link Road








WBM - II & III



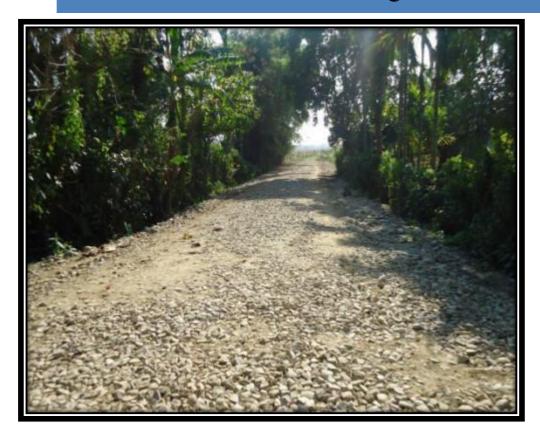



WBM at Innao Khamti Link Road

WBM at IRBn HQ Link Road







RCC Culvert 1m span at IRBn HQ. Link Road

RCC Culvert - 1m Span at Mokrun Link Road







RCC Culvert - 1m Span at Innao Khamti Link Road

RCC Culvert- 1m Span at New Township Internal Road







RCC Culvert- 1m Span at Sompoi Link Road

RCC Box Culvert- 1.00 mtr. Span at Innao Link Road





RCC Culvert 6m span at Mokrun Link Road




NAME OF PROJECT: C/o Approach Road from CO Hq. Dadam to Muktowa-II

SANCTION NO. & DATE: NB.AR/629/SPD-3/2015-16, dated. 04/12/2015

For Rs. 1920 lakhs (CS: Rs. 1728 lakhs & SS: Rs. 192 lakhs)

(Financial figures in lakhs)

Cumulative Funds Released		Scope of W	Progressive Achievement upto 03/ 2018		Target 2018-19		Achievement during 2018-19		Cumulative Achievement upto 03/2019		UC Status/ Remarks		
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC(2016-17)	900.00	1) Formation cutting (5.95 mtr width)- 12.50 Km	6.96	6.96	12.50								
LC(2017-18)	620.00	2) Slab Culvert 2m- 30 Nos	8.47		27		3	 0.00 207.09					UC submitted Rs. 1414.22 lakhs Physical targets for 100% completion within 2018-
LC(2018-19)	207.09	3) Slab Culvert 4m- 4 Nos	14.20	1920.00	4								
Total	1727.09	4) Slab Culvert 6m- 2 Nos	22.90		2								
		5) R/Wall 3 Mtr Ht 200.00 mtr	0.40		70.00	1414.00	130.00						
Fund surrender drg 2017-18	105.78	6) B/Wall 3.3 mtr ht- 180.00 mtr	0.37		180.00	1414.22							
urg 2017 10	1621.31	31 7) GSB-I-12.412 Km	15.86	1	12.41								19 in anticipation
		8) WBM-II- 12.412 Km	12.54	-	11.00		1.42					_	of balance funds release.
		9) WBM-III- 12.412 Km	12.65		6.00		6.41			_		-	
		10) Black topping- 12.50 Km	14.99		6.00		6.50						
		11) Pucca Drain- 7.45 Km	0.0022				7.45						

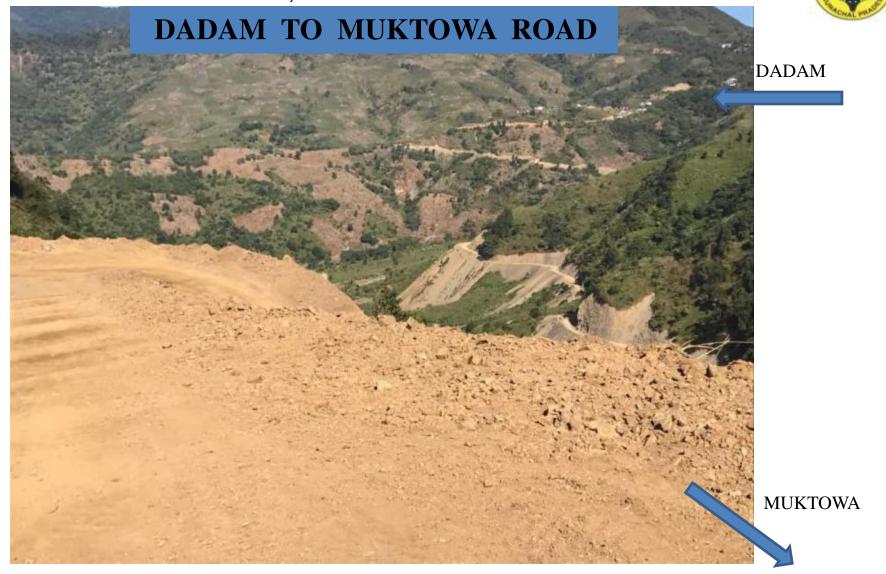

VIEW OF THE ALIGNMENT





VIEW OF THE ALIGNMENT

DADAM





CH-3.600 KM






CH-2.000 KM




CH-6.000 KM

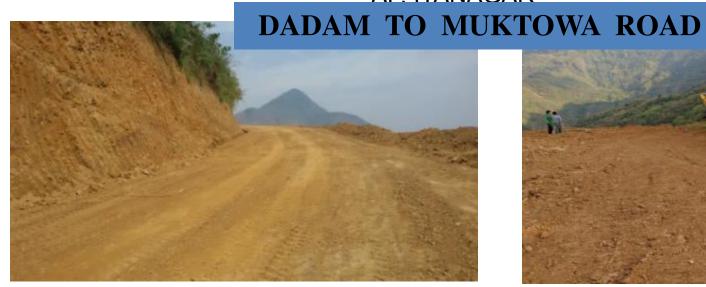

Ch-8.000 Km



Ch-12.000 Km

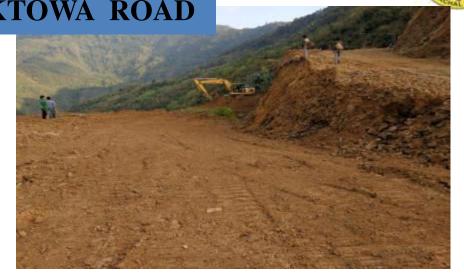

CH-10.500 Km



Formation Cutting

Ch-12.500 Km







GSB at Ch-4.000 Km



GSB at Ch-5.000 Km



GSB at Ch-4.500 Km



GSB at Ch- 6.500 Km



WBM-II at Ch-0.500 Km



Breast Wall - Ch-1.600 Km



WBM-II at Ch-1.50 Km



Breast wall - Ch-3.400 Km
















BT at Starting point



BT at Ch- 4.000 Km





B/wall at Ch-7.800 Km

B/wall at Ch-3.400 Km



S/Cul 4m span Ch-1.600 km



S/Cul 2m span Ch-1.300 Km



S/Cul 4m span Ch-1.900 Km



S/Cul 2m span Ch-1.940 Km



S/Cul 2m span Ch-4.700 Km

NAME OF PROJECT : C/o RCC Bridge (Span 24 Mtr) at 11 Km on Wakro-Deban road in Wakro Circle, Namsai District

SANCTION NO. & DATE: NB.AR/579/SPD-3/2015-16, dated. 28/12/2015

For Rs. 300 lakhs (CS : Rs. 270 lakhs & SS : Rs. 30 lakhs)

(Financial figures in lakhs)

Cumulative Funds Released		Scope of Works			Progressive Achievement upto 03/ 2018		Target 2018-19		Achievement during 2018-19		Cumulative Achievement upto 03/2019		UC Status/ Remarks	
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin		
LC (2016- 17)	150.00	1) RCC Bridge (24.00 mtr span)- 1 Nos		300.00	Bridge- 100% compltd.	287.10	100% Completion (Liability	12.90						
LC (2017- 18)	120.00				& approach road in progress		clearance)						UC	
SS (2017-18)	17.10												submitted Rs. 287.10 lakhs	
Total	287.10													



Construction of RCC Bridge at 11 Km on Wakro Deban road in Wakro circle.



Bridge Completed, Approach road in progress



NAME OF PROJECT: C/o Road from Votnu village to Khanu village, Wakka Circle

SANCTION NO. & DATE: NB.AR/882/SPD-3/2015-16, dated. 11/03/2016

For Rs. 800 lakhs (CS : Rs. 720 lakhs & SS : Rs. 80 lakhs)


(Financial figures in lakhs)

Cumulative Release		Scope of Wo	orks		_	ressive nent upto 2018	Target 2	2018-19	Achiev during 2		Cumu Achiev	llative vement 3/2019	UC Status/ Remarks
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2016-17)	350.00	Widening- 6.00 Km	15.33		6.00								
LC (2017-18)	300.00	S/cul 1.50 m span- 9 Nos	7.75		9								
LC (2018-19)	70.00	S/cul 2.00 m span- 7 Nos	10.33		7								UC
Fotal	720.00	S/cul 6.00 m span- 1 No	/wall (4.00 mtr ht.)- 0.48		650								submitted Rs. 650.00 lakhs Full balance physical target kept
		R/wall (4.00 mtr ht.)- 70.00 mtr					70.00						
		B/wall (3.00 mtr ht.)- 25 mtr	0.38			650.00	25.00	70.00					
		Sub Grade-6.465 Km	2.97	91	6.47								
		GSB - I- 6.465 Km	18.91		6.45								in anticipation of receipt o
		WBM-II- 6.465 Km	17.22		6.45								state share
		WBM-III- 6.465 Km	17.32		6.465								
		BT- 6.465 Km	16.22		2.00		4.46						



C/o Road from Votnu village to Khanu



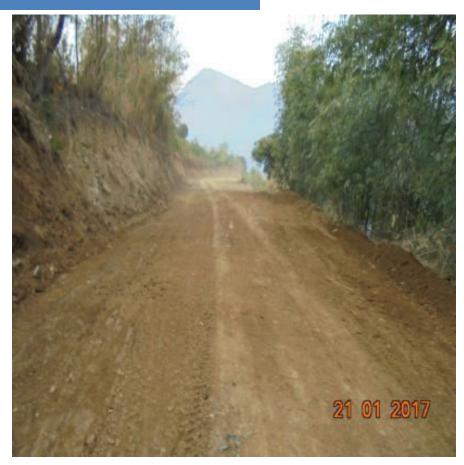

Ch: 0.350 km Formation Cutting

CH: 5.00 KM



C/o Road from Votnu village to Khanu






WBM







The same of the sa

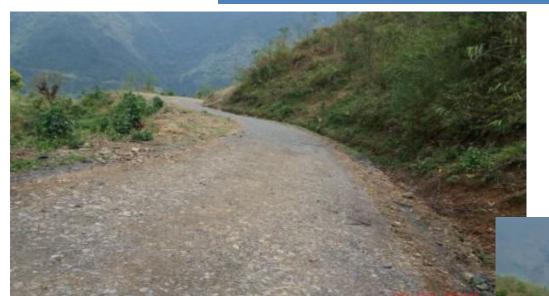

CH- 0.320 KM



CH-1.720 KM







CH-5.780 KM



C/o Road from Votnu village to Khanu



CH: 0.120 KM



СН-0.650км

CARPETING



C/o Road from Votnu village to Khanu



CH- 1.980KM

CARPETING



C/o Road from Votnu village to Khanu





CH: 4.650 KM



C/o Road from Votnu village to Khanu



2.00 MTR SPAN AT CH: 3.550 KM



6.00 MTR SPAN at Ch: 3.600 km

SLAB CULVERT





1.500 mtr. Span Culvert at Ch:- 2.200 Km



4.00 mtr. Span Culvert at Ch:- 2.950 Km

PUBLIC WORKS DEPARTMENT





Phase I: 0 to 5 Kms

SANCTION NO. & DATE: NB.AR/882/SPD-3/2015-16, dated. 11/03/2016

For Rs. 1000 lakhs (CS: Rs. 900 lakhs & SS: Rs. 100 lakhs)
(Financial figures in lakhs)

Cumulative Release		Scope of Wo	orks		Progr Achieven 03/2	nent upto	Target :	2018-19	Achiev during		Achie	vement 3/2019	UC Status/ Remarks
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2016- 17)	400.00	Formation Cutting- 5.00 Km	42.14		5.00								UC submitted Rs. 854.00 lakhs Full balance physical target kept in
LC (2017- 18)	654.00	GSB - I- 4.97 Km	24.08		4.97								
LC(2018-19)	46.00	WBM-II- 4.97 Km	17.77		4.50		0.48						
Fund surrendered during 2017-18	200.00	WBM-III- 4.97 Km	19.53	.33 .56	3.00	854.00	1.97						
Total	900.00	BT- 4.97 Km	20.87				4.97	46.00					
		R/wall (3.00 mtr ht.)- 130.00 Mtr	0.33		130.00								
		B/Wall (2 mtr ht.)- 74.00 mtr	0.56		74.00								anticipation of receipt of state share
		S/cul 1.50 m span- 12 Nos	8.23		12								
		CC Drain- 4.97 Km	2.50		4.50		0.47						

C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km




Ch: 0.630 Km

Formation Cutting



Ch: 4.100 Km

C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km

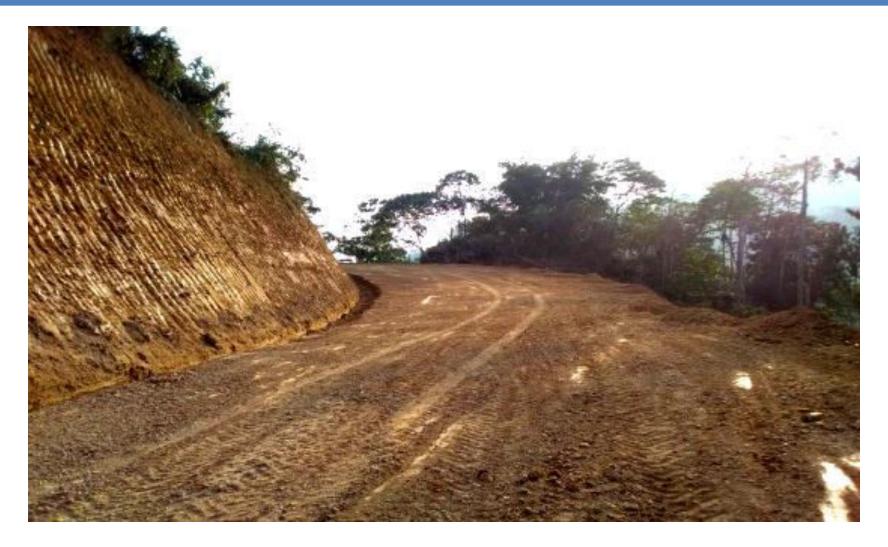

Formation Cutting



C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km



Ch: 1.820 Km

Slab Culvert 1.5 Mtr. SPAN



Ch: 3.435 Km

C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km



Slab Culvert 1.5 Mtr. (Ch: 3.780 Km)



CC Drain (Ch: 2.230 Km)



C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km



GSBC-I (Ch: 4.350 Km)



GSBC-I (Ch: 3.180 Km)

GSBC



C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km



Ch: 1.470 Km

C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km



WBM-III (Ch: 1.200 Km)



C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km





(Ch: 0.020 Km) (Ch: 0.050 Km)

RETAINING WALL



C/o Road from Chattong to Kamnu via Chopsa (15.00 km) Ph I: 0 – 5 Km



Ch: 1.150Km

BREAST WALLS



Ch: 2.280 Km



RIDF-XXII (2016-17)

- 1. C/o Road & Bridge from Emphum to Lunka village via Munglang village in Namsai District (10km)
- 2. C/o Road Laiwang to Thungjang via Tutnyu village in Tirap Distt
- 3. <u>C/o School Infrastructure Govt. Higher Sec. School at Dambuk in</u>
 Lower Dibang Valley



NAME OF PROJECT: C/o Road & Bridge from Emphum to Lunka village via Munglang village (10km)

SANCTION NO. & DATE : PD(PP&M)/RIDF-1/14-15(Pt-IX) Dtd 30/1/17

For Rs. 1100 lakhs (CS: Rs. 990 lakhs & SS: Rs. 110 lakhs)
(Financial figures in lakhs)

Cumulative Funds Released		Scope of Works			Progressive Achievement upto 03/ 2018		Target 2018-19		Achievement during 2018-19		Cumulative Achievement upto 03/2019		UC Status/ Remarks	
		Phy	Rate	Fin	Phy	ıy Fin	Phy	Phy Fin	Phy	Fin	Phy	Fin		
LC (2017-18)	297.00	Earth work- 4.25 Km	11.10		4.25									
LC (2018-19)	310.20	GSB- 10.00 Km	19.78		10.00								UC submitted Rs. 297.00 lakhs	
Total	607.20	WBM- II- 10.00 Km	16.78		4.00	297.00	6							
		WBM- III- 10.00 Km	12.69	1100.00			5.00	310.20						
		Carpetting- 10.00 Km	15.94				5.00							
		S/cul 1.50 m span- 11 Nos	6.62		10		1							
		S/cul 2.00 m span- 10 Nos	11.56		4		2							
		S/cul 4.00 m span- 2 Nos	20.97				2							
		RCC bridge 24.00 m span- 1 No	164.62											



C/o Road & Bridge from Emphum to Lunka village via Munglang village (10km)



Earth work at Ch. 0.00 to 1.00 Km



Earth work at Ch. 2.00 to 3.00 Km



C/o Road & Bridge from Emphum to Lunka village via Munglang village (10km)



WBM-III at Ch. 0.00 to 2.00 Km



RCC S/Cul-2m span at Ch. 0.60 Km



NAME OF PROJECT: C/o Road Laiwang to Thungjang via Tutnyu village

SANCTION NO. & DATE : PD(PP&M)/RIDF-1/14-15(Pt-X) Dtd 30/1/17

For Rs. 1400 lakhs (CS: Rs. 1260 lakhs & SS: Rs. 140 lakhs) (Financial figures in lakhs)

Cumulative Releas		Scope of Works			Progre Achievem 03/ 2	ent upto	Target	Target 2018-19 Achievement during 2018-19		Achiev	lative vement 3/2019	UC Status/ Remarks	
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC(2017- 18)	378.00	F/Cutting- 7.50 Km	42.30		3.60		3.90						
LC(2018- 19)	372.24	GSB- 7.44 Km	20.40				3.50	-					
Fund surrendered during 2017-18	238.00	WBM- II- 7.44 Km	15.69										UC submitted
Total	512.24	WBM- III- 7.44 Km	15.80			140.00		272.24					
		Black topping- 7.44 Km	16.78										
		Slab culverts	-	1400.00	-	140.00		372.24					Rs. 140.00
		a) 1.5 mtr- 8 Nos	10.06		2		6						lakhs
		b) 2.0 mtr- 12 Nos	10.34		3		9						
		c) 4.0 mtr- 3 Nos	16.91				2						
		d) 6.0 mtr- 3 Nos	25.73				2						
		R/ Wall- 112.50 mtr	0.47										
		B/ Wall- 96.00 mtr	0.44										
		Pucca drain- 2230.20 mtr	0.03										

A CONAL PROPERTY.

C/o Road Laiwang to Thungjang via Tutnyu village



Formation cutting at Ch-0.000 Km



Slab Culvert (2m span) at Ch-0.210 Km



Formation cutting at Ch-2.5000 Km



Slab Culvert (2m span) at Ch-0.670 Km



C/o Road Laiwang to Thungjang via Tutnyu village



Slab Culvert (2m span) at Ch-1.080 Km



Slab Culvert (2m span) at Ch-1.290 Km

NAME OF PROJECT: C/o School Infrastructure Govt. Higher Sec. School at Dambuk in Lower Dibang Valley

SANCTION NO. & DATE: PP&M/RIDF-3/Fund/14-15(Pt-VI) Dtd 24/1217

For Rs. 1000 lakhs (CS: Rs 894.15 lakhs & SS: Rs. 105.85 lakhs)

Cumulativ Release		Scope of W	orks/		Progress Achievement 2018	upto 03/	Target 20)18-19	Achiever during 20			lative vement 3/2019	UC Status/ Remarks
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2017- 18)	268.25	School building- 2535 Sqm	720.51		Site development compltd.		50%		Foundatio n work in progress				UC
LC(2018-19)	283.80	T- III Qtr- 2 Nos	23.70				Upto roof level						submitted Rs. 40.00 lakhs
Fund surrendered during 2017-18	228.25	T- II Qtr- 2 Nos	18.31	1000.00		40.00	Upto roof level	283.80					Due to delay in finalization
Total	323.80	T- I Qtr- 2 Nos	16.31				Upto roof level						of land, the target could not be
		Boundary wall- 700.65 mtr	0.14										achieved



C/o School Infrastructure Govt. Higher Sec. School at Dambuk in Lower Dibang Valley



Site Development



RIDF- XXIII (2017-18)

- C/o Dambuk-Paglam road (SH: River training work, Composite bridge (30 m span) on Sissar river & RCC Cell Box Culvert (3x3 m) in L/Dibang Valley Distt
- 2. C/o Road from Kamlang Nagar to Kathan in Lohit Distt
- 3. C/o Road from PMGSY Point Lyngok to Tirap sakan village in Changlang Dist
- 4. C/o Road from Jonghihavi to Songkhuhavi in Changlang Distt
- 5. C/o CC pavement road i/c drainage/footpath & railing in Changlang township
- 6. C/o Road from Chattong to Kamnu via Chopsa(5-12 Km) (Ph-II) in Longding District
- 7. C/o Road from Hukanjuiri-Namsang-Deomali in Tirap District.



NAME OF PROJECT: C/o Road from Kamlang Nagar to Kathan in Lohit Distt

SANCTION NO. & DATE: FIN/EA-261/2016 (Pt-III)/310 Dtd. 06/02/2018

For Rs. 1000 lakhs (CS: Rs 900.00 lakhs & SS: Rs. 100.00 lakhs)

Cumulative Fu	nds Released	Scope of Wo	orks		Achieven	ressive nent upto 2018	Target	2018-19	Achiev during 2		Achiev	lative vement 3/2019	UC Status/ Remarks
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Tremai is
LC (2017-18)	270.00	Widening- 0.41 Km	0.02				0.41						
LC (2018-19)	200.00	GSB- 2.00 Km	16.04	-			2.00	-				_	
Fund surrendered drg 2017-18	270.00	WBM- II- 2.30 Km	14.20				2.30						
Total	200.00	WBM- III- 20.00 Km	8.22				2.30	1					
		Carpeting- 20.00 Km	14.45				1.50						
		Retaining Wall - a) 3.00 m (h)- 140.00 mtr b) 4.00 m (h)- 110.00 mtr c) 5.00 m (h)- 160.00 mtr	0.26 0.39 0.55	1000.00		- 	50.00 30.00	200.00					
		Breast Wall a) 3.00 m (h)- 20.00 mtr b) 4.00 m (h)- 65.00 mtr	- 0.26 0.38				- 						
		S/Cul- 2.00 m span- 13 Nos	10.60										
		S/Cul- 6.00 m span- 2 Nos	24.20										



NAME OF PROJECT : C/o Road from PMGSY Point Lyngok to Tirap Sakan village in Changlang Distt

SANCTION NO. & DATE: NBAR/1245/SPD-3/2017-18, dated. 01/03/2018,

For Rs. 980.00 lakhs (CS: Rs. 882.00 lakhs & SS: Rs. 98.00 lakhs)

Cumulative Release		Scope of V	Vorks	03/ 2018		Target	2018-19	Achievement during 2018-19		Cumulative Achievement upto 03/2019		UC Status/ Remarks	
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2018-19)	108.00	F/ Cutting- 12.10 Km	49.48				2.00						
SS (2018-19)	0.00	Slab culvert 2 m span- 15 Nos	9.27										
Total	108.00	Slab culvert 4 m span- 3 Nos	21.30	980.00				108.00					
		R/ Wall- 3 m Ht 250.00 m	m Ht 0.42										



NAME OF PROJECT: C/o Road from Jonghihavi to Songkhuhavi in Changlang Distt

SANCTION NO. & DATE: NB.SPD/1192/RIDF-XXIII(Ar.P)/169PSC/2017-18 Dtd 8/2/18

For Rs. 1000.00 lakhs (CS: Rs. 900.00 lakhs & SS: Rs. 100.00 lakhs)

Cumulative Release		Scope of W	orks		Achieven	essive nent upto 2018	Target	2018-19	Achiev during 2		Achiev	vement 3/2019	UC Status/ Remarks
	1	Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2017-18)	270.00	Widening- 0.48 Km	26.29				0.48					-	
LC (2018-19)		Slab culvert 2 m span- 14 Nos	8.54				9	_					
Fund surrendered drg 2017-18	270.00	R & B Wall- 222.00 mtr	0.50										
Total	200.00	GSB- 9.95 Km	23.96	1000.00			9.95	200.00					
		WMM- 9.95 Km	26.81							-		1	
		CC Drain- 9.95 Km	18.54							-			
		W. Beam Crash Barrier- 235.00 mtr	0.04										



NAME OF PROJECT: C/o CC pavement road i/c drainage/footpath & railing in Changlang township

SANCTION NO. & DATE: NB.SPD/1282/RIDF-XXIII(Ar.P)/170PSC/2017-18 Dtd 09/03/2018

For Rs. 1000.00 lakhs (CS: Rs. 900.00 lakhs & SS: Rs. 100.00 lakhs)

Cumulative Release		Scope of W	orks		Progr Achieven 03/2	nent upto	Target	2018-19	Achiev during 2		Cumu Achiev upto 0	ement	UC Status/ Remarks
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	
LC (2018- 19)	200.00	Widening- 1.23 Km	26.28				1.23						
SS (2018-19)	0.00	Embankment- 0.35 Km	11.24	1			0.35						
Total	200.00	Slab culvert 1.50 m span- 6 Nos	10.60				3						
		Slab culvert 2.00 m span- 3 Nos	13.02	1000.00			3						
		Slab culvert 4.00 m span- 2 Nos	21.53					200.00					
		R/ Wall- 480.00 mtr	0.40										
		B/ Wall- 170.00 mtr	0.23	1			120.00			-			
		CC Road (2 lane)- 1.83 km	258.85				0.48						
		CC Drain with cover- 1650.00 mtr	0.04										



NAME OF PROJECT : C/o Road from Chattong to Kamnu via Chopsa(5-12 Km) (Ph-II)

in Longding District

SANCTION NO. & DATE: NB.SPD/1192/RIDF-XXIII(Ar.P)/169PSC/2017-18 Dtd 8/2/18

For Rs. 700.00 lakhs (CS: Rs. 6300.00 lakhs & SS: Rs. 70.00 lakhs)

Cumulative Releas		Scope of W	orks		Progressive Achievement upto 03/ 2018		Target 2018-19		Achievement during 2018-19		Cumulative Achievement upto 03/2019		UC Status/ Remarks		
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin			
LC (2017-18)	189.00	F/ Cutting- 2.10 Km	43.06				2.00								
LC (2018-19)	120.00	Slab culvert (1.50 mtr span)- 7 Nos	9.62				4	_		_					
Fund surrendered drg 2017-18	189.00	GSB- 2.04 Km	36.37												
Total	120.00	WBM- II- 2.04 km	18.32									-			
		WBM- III- 2.04	19.76	700.00	700.00	700.00				120.00					
		Black Topping- 2.04 Km	22.94					_							
		R& B Wall- 47.00 mtr	0.43												
		Bailey Bridge (120 Ft span)- 1 No	228.24												
		CC Drain- 2.04 Km	32.88												



NAME OF PROJECT: C/o Road from Hukanjuri-Namsang-Deomali (12 Km), in Tirap District

SANCTION NO. & DATE: NB.SPD/1282/RIDF-XXIII/(Ar.P)/170PSC/2017-18 Dtd 09/03/2018

For Rs. 3000.00 lakhs (CS: Rs. 2700.00 lakhs & SS: Rs. 300.00 lakhs)

Cumulative Releas		Scope of W	Progr Achieven 03/2	nent upto	Target	2018-19	Achiev during 2		Achiev	lative vement 3/2019	UC Status/ Remarks		
		Phy	Rate	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Phy	Fin	Kemarks
LC (2018-19)	320.00	Widening- 0.48 Km	15.43				0.48						
SS (2018-19)	0.00	Formation cutting- 5.52 Km	33.44				5.52						
Total	320.00	Embankment filling- 6.00 Km	25.04				6.00						
		Slab culvert 2 m span- 11 Nos	11.36										
		Slab culvert 4 m span- 4 Nos	21.48										
		Slab culvert 6 m span- 1 No	30.42					320.00					
		R& B Wall- 360.00 mtr	0.38										
		GSB- 11.84 Km	25.90									1	
		WMM- 11.84 Km	32.42									1	
		DBM & BC- 12.00 Km	45.53			1				-		1	
		CC Drain- 6460.00 mtr	0.03			1				-		1	
		RCC bridge (60.00 mtr span)- 1 No	440.12										
		RCC bridge (30.00 mtr span)- 1 No	241.39										
